

A woman with blonde hair and glasses, wearing a patterned blouse and dark trousers, stands and presents to a group of people seated in a modern office. She holds a small object in her right hand and gestures with her left. The audience, consisting of several men and women, is seated and listening attentively. The room has large windows in the background, showing a cityscape. The overall atmosphere is professional and collaborative.

УПРАВЛЕНИЕ КОММУНИКАЦИЯМИ ПРОЕКТА



Knowledge Areas	Project Management Process Groups				
	Initiating	Planning	Executing	Monitoring and Controlling	Closing
4. Project Integration Management	4.1 Develop Project Charter	4.2 Develop Project Management Plan	4.3 Direct and Manage Project Work 4.4 Manage Project Knowledge	4.5 Monitor and Control Project Work 4.6 Perform Integrated Change Control	4.7 Close Project or Phase
5. Project Scope Management		5.1 Plan Scope Management 5.2 Collect Requirements 5.3 Define Scope 5.4 Create WBS		5.5 Validate Scope 5.6 Control Scope	
6. Project Schedule Management		6.1 Plan Schedule Management 6.2 Define Activities 6.3 Sequence Activities 6.4 Estimate Activity Durations 6.5 Develop Schedule		6.6 Control Schedule	
7. Project Cost Management		7.1 Plan Cost Management 7.2 Estimate Costs 7.3 Determine Budget		7.4 Control Costs	
8. Project Quality Management		8.1 Plan Quality Management	8.2 Manage Quality	8.3 Control Quality	
9. Project Resource Management		9.1 Plan Resource Management 9.2 Estimate Activity Resources	9.3 Acquire Resources 9.4 Develop Team 9.5 Manage Team	9.6 Control Resources	
10. Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 Monitor Communications	
11. Project Risk Management		11.1 Plan Risk Management 11.2 Identify Risks 11.3 Perform Qualitative Risk Analysis 11.4 Perform Quantitative Risk Analysis 11.5 Plan Risk Responses	11.6 Implement Risk Responses	11.7 Monitor Risks	
12. Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
13. Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder Engagement	13.3 Manage Stakeholder Engagement	13.4 Monitor Stakeholder Engagement	



Процессы управления коммуникациями



- ❖ Планирование управления коммуникациями
- ❖ Управление коммуникациями
- ❖ Мониторинг коммуникаций





Планирование управления коммуникациями

- ❖ План управления коммуникациями
- ❖ План вовлечения заинтересованных сторон.



План коммуникаций:

- ❖ Введение
- ❖ Методы коммуникации
- ❖ Инструменты
- ❖ Записи
- ❖ Отчетность
- ❖ Сроки
- ❖ Роли и ответственности
- ❖ Список заинтересованных сторон
- ❖ Информация, необходимая для каждой заинтересованной стороны
- ❖ Процедуры эскалации.
- ❖ др.



Communication Matrix



Meeting	Duration	Frequency	Purpose	Meeting channel	Stakeholders Participants List	Team Participants List
Project Kickoff Meeting						
Project Status Meeting						
Hand-shake meeting						
Stakeholder Meetings						
Change Control Meetings						
Project Review Meeting						
Problem Solving Meetings						
Team Building Meetings						
Decision Making Meetings						
....						



Communication Matrix



Communication	Frequency	Goal	Owner	Audience
Email				
Project status report	Weekly	Review project status and discuss potential issues or delays	Project manager	Project team + project sponsor
Meetings				
Team standup	Daily	Discuss what each team member did yesterday, what they'll do today, and any blockers	Project manager	Project team
Project review	At milestones	Present project deliverables, gather feedback, and discuss next steps	Project manager	Project team + project sponsor
Post-mortem meeting	At end of project	Assess what worked and what did not work and discuss actionable takeaways	Project manager	Project team
TeamGantt				
Task progress updates	Daily	Share daily progress made on project tasks	Project manager	Project team



Communication Matrix



Audience

- Team
- Stakeholders

Message Type

- E-mail
- Face-to-face

Delivery Method

- Meeting
- Presentation

Schedule

- Daily
- Weekly

Owner

- Project Manager
- Product Owner







Escalation Procedures

Level 3	Cost, billing, resources, contract issues + issues not resolved by levels 1 and 2	Contact(s)	Contact(s)
Level 2	Design issues, collaboration between vendors + issues not resolved by level 1	Contact(s)	Contact(s)
Level 1	Operational issues, scope and schedule issues	Contact(s)	Contact(s)



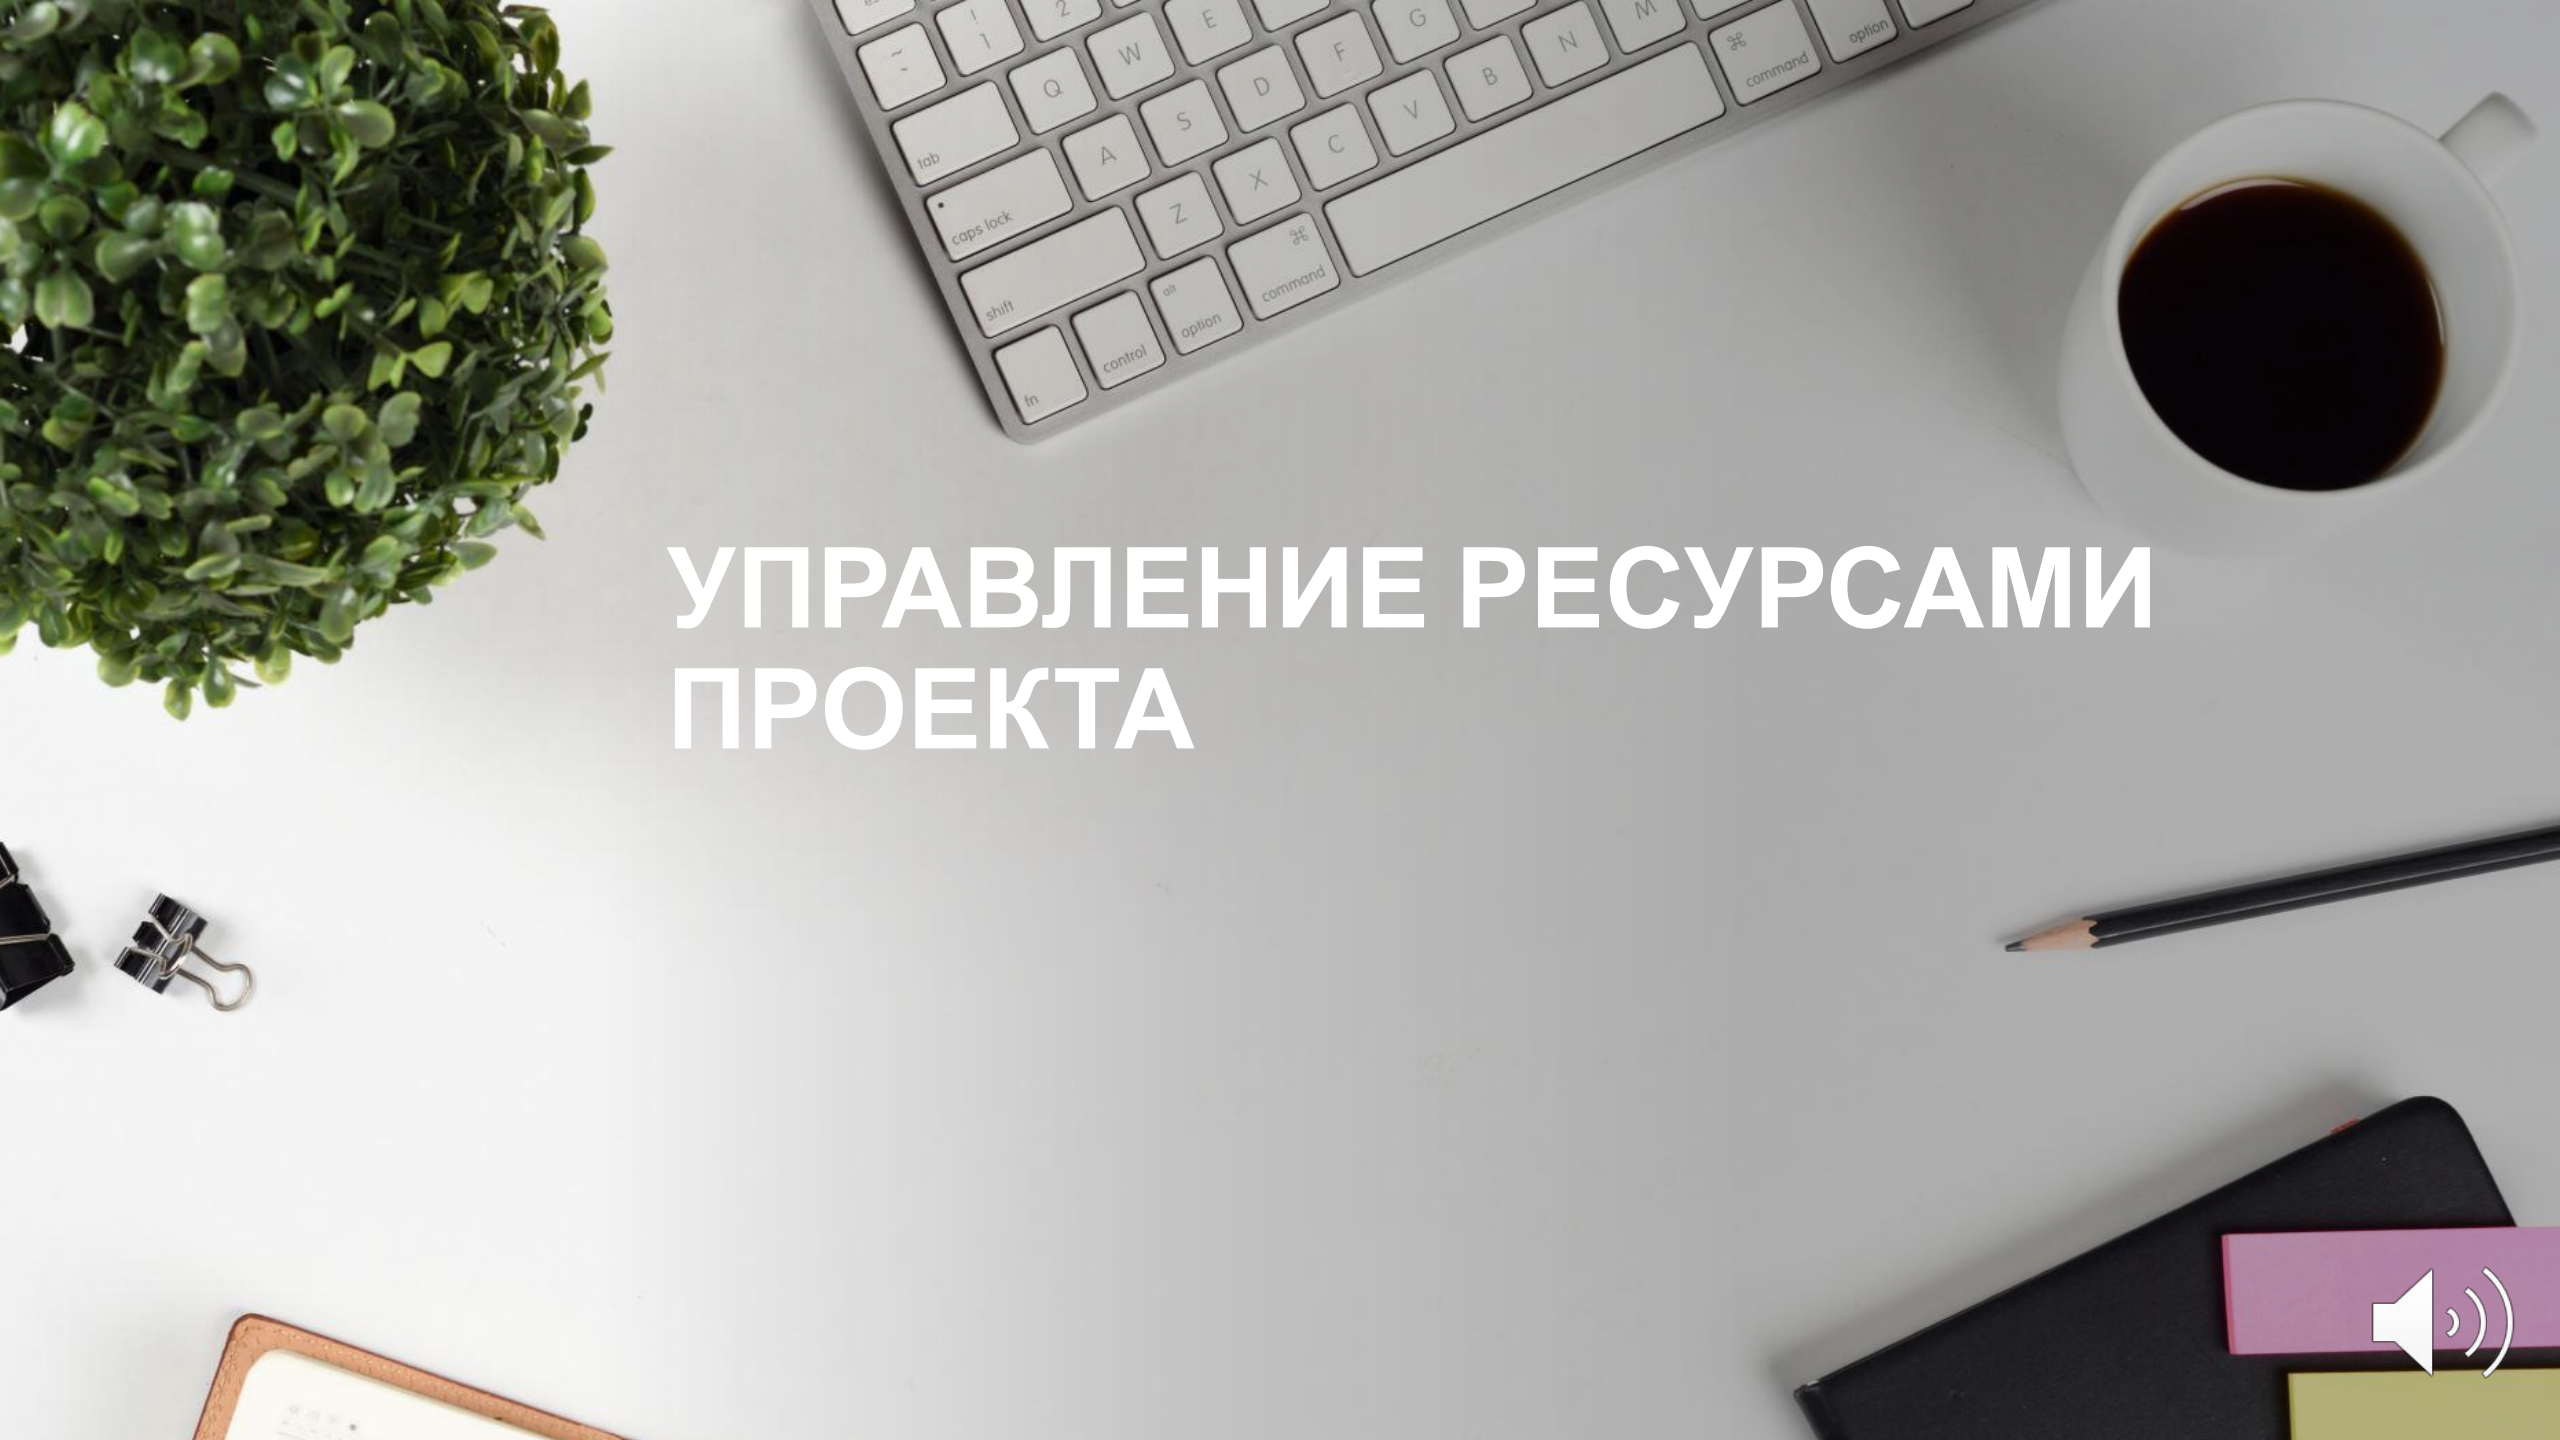

УПРАВЛЕНИЕ РЕСУРСАМИ ПРОЕКТА



Knowledge Areas	Project Management Process Groups				
	Initiating	Planning	Executing	Monitoring and Controlling	Closing
4. Project Integration Management	4.1 Develop Project Charter	4.2 Develop Project Management Plan	4.3 Direct and Manage Project Work 4.4 Manage Project Knowledge	4.5 Monitor and Control Project Work 4.6 Perform Integrated Change Control	4.7 Close Project or Phase
5. Project Scope Management		5.1 Plan Scope Management 5.2 Collect Requirements 5.3 Define Scope 5.4 Create WBS		5.5 Validate Scope 5.6 Control Scope	
6. Project Schedule Management		6.1 Plan Schedule Management 6.2 Define Activities 6.3 Sequence Activities 6.4 Estimate Activity Durations 6.5 Develop Schedule		6.6 Control Schedule	
7. Project Cost Management		7.1 Plan Cost Management 7.2 Estimate Costs 7.3 Determine Budget		7.4 Control Costs	
8. Project Quality Management		8.1 Plan Quality Management	8.2 Manage Quality	8.3 Control Quality	
9. Project Resource Management		9.1 Plan Resource Management 9.2 Estimate Activity Resources	9.3 Acquire Resources 9.4 Develop Team 9.5 Manage Team	9.6 Control Resources	
10. Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 Monitor Communications	
11. Project Risk Management		11.1 Plan Risk Management 11.2 Identify Risks 11.3 Perform Qualitative Risk Analysis 11.4 Perform Quantitative Risk Analysis 11.5 Plan Risk Responses	11.6 Implement Risk Responses	11.7 Monitor Risks	
12. Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
13. Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder Engagement	13.3 Manage Stakeholder Engagement	13.4 Monitor Stakeholder Engagement	




Управление ресурсами проекта

- ❖ Планирование управления ресурсами
- ❖ Оценка ресурсов операции
- ❖ Приобретение ресурсов.
- ❖ Развитие команды
- ❖ Управление командой
- ❖ Контроль ресурсов




В чем разница?

- управлять ресурсами команды
- управлять материальными ресурсами.

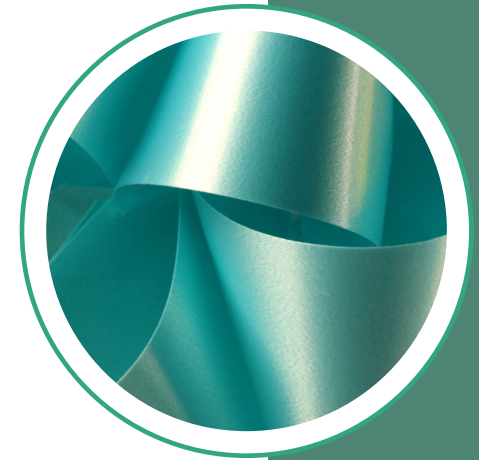


Ключевые концепции управления ресурсами проекта

- ❖ Команда выполняет совместную работу
- ❖ Руководитель должен тратить время на команду.
- ❖ Участие каждого и всех ценно для проекта.
- ❖ Использование опыта каждого при планировании.

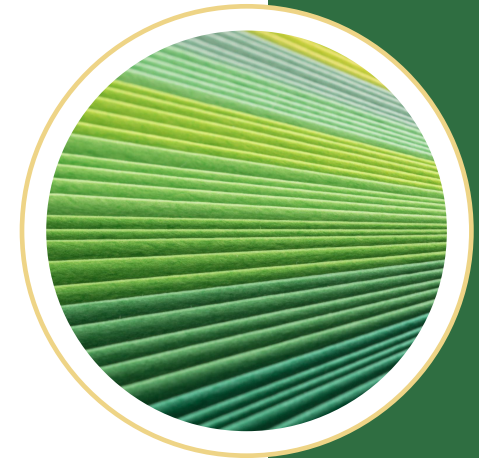

Руководитель проекта - лидер и руководитель команды проекта.

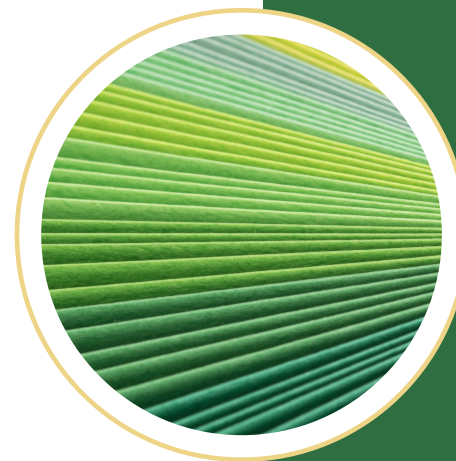

Тенденции и практики в управления ресурсами проекта

Методы управления ресурсами. Дефицит ресурсов породил методы

- бережливого менеджмента (LEAN),
- производства «строго в срок» (just-in-time, JIT),
- кайзен (Kaizen),
- всеобщего обслуживания оборудования (total productive maintenance, TPM)

Эмоциональный интеллект (emotional intelligence, EI).

Самоорганизующиеся команды.

Виртуальные команды/распределенные команды.



Планирование управления ресурсами

Планирование управления ресурсами — это процесс, определяющий, каким образом осуществлять оценку, приобретение, управление и использование кадровых и материальных ресурсов команды.



Оценка ресурсов операции

это процесс оценки ресурсов команды, типа и количества материала, оборудования и расходных материалов, необходимых для выполнения работ проекта.



Приобретение ресурсов

Команда управления проектом может иметь или не иметь прямого контроля при выборе ресурса



Критерии выбора

- ❖ Доступность
- ❖ Стоимость
- ❖ Способность
- ❖ Опыт
- ❖ Знания
- ❖ Навыки
- ❖ Отношение
- ❖ Международные факторы



Организационная структура проекта (Organizational Breakdown Structure, OBS)

соответствующая проекту временная организационная структура, включающая всех его участников и создаваемая для успешного управления и достижения целей проекта.




Организационная структура проекта (Organizational Breakdown Structure, OBS)



Матрица ответственности (Responsibility Assignment Matrix, RAM)

RAM - структура, приводящая организационную иерархическую структуру проекта в соответствие с иерархической структурой работ и помогающая обеспечить назначение для каждого элемента содержания работ по проекту ответственного лица или команды.

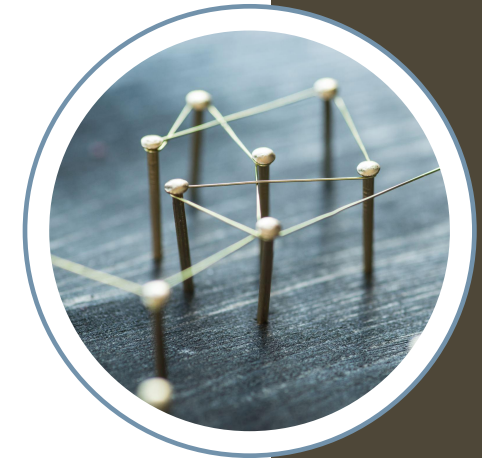

Responsibility Accountability RACI Matrix

Role	Executive Sponsor	Project Sponsor	Steering Committee	Advisory Committee	Role #5	Project Manager	Tech Lead	Functional Lead	SME	Project Team Member	Developer	Administrative Support	Business Analyst	Role #4	Role #5	Consultant	PMO	Role#3	Role#4	Text Here
Project Deliverable (or Activity)	Project Leadership					Project Team Members					Project Sub-Team					External Resources				
Initiate Phase Activates																				
Request Review by PMO	A/C	R/A				R/A	A/C		C											
Submit Project Request						R											A			
Research Solution	I					R/A	A/C	A/C	C				C			C				
Develop business Case	I	A/C	I	I		R/A	C	C	C				C			C	C			
Plan phase Activities																				
Create Project Charter	C	C				R/A	C	C	C				C			C				
Create Schedule	I	I	I	I		R/A	C	C	C	C	C	C	C			C	I			
Create Additional Plans as Required	I	I	I			R/A				I	I	I	I			C	I			
Execute phase Activities																				
Build Deliverables	C/I	C/I	C/I	C/I			R/A	R/A	R/A	R/A	R/A					A/C				
Create Status Report	I	I	I	I		R/A	R/A	R/A	R/A							C	I			
Control phase Activities																				
Perform change Management		C	C	C		R	A	A	A							C	I			
Close phase Activities																				
Create Lessons Learned	C	C	C	C		R/A	C	C	C	C	C	C	C			C	C			
Create Project Closure Report	I	I	I	I		R/A	I	I	I	I	I	I	I				I			





- Responsible
- Accountable
- Consulted
- Informed

	Frodo	Sam	Gandalf	Aragorn	Head of Elves (Elrond)
Decide on what to do with ring	C	I	A	C	R
Create Fellowship	R	C	A	C	R
Get the ring to Mt Doom	R	C	A	C	I
Distract and defeat enemies	I	R	C	R	I



Развитие команды

Руководители проектов должны создать среду, которая способствует **командной работе** и постоянно **мотивирует** команду, ставя перед ней **вызовы** и создавая благоприятные **возможности**



Цели развития команды проекта

- ❖ повышение уровня знаний и навыков
- ❖ повышение чувства доверия и единодушия
- ❖ создание здоровой рабочей культуры в команде
- ❖ наделение команды полномочиями



Что сделать дома

- по свежим следам сделайте в дипломном проекте план план управления коммуникациями и план управления ресурсами (плюс закупками)
