





PROCESS GROUP AND KNOWLEDGE AREA MAPPING


Knowledge Areas	Project Management Process Groups				
	Initiating	Planning	Executing	Monitoring and Controlling	Closing
4. Project Integration Management	4.1 Develop Project Charter	4.2 Develop Project Management Plan	4.3 Direct and Manage Project Work 4.4 Manage Project Knowledge	4.5 Monitor and Control Project Work 4.6 Perform Integrated Change Control	4.7 Close Project or Phase
5. Project Scope Management		5.1 Plan Scope Management 5.2 Collect Requirements 5.3 Define Scope 5.4 Create WBS		5.5 Validate Scope 5.6 Control Scope	
6. Project Schedule Management		6.1 Plan Schedule Management 6.2 Define Activities 6.3 Sequence Activities 6.4 Estimate Activity Durations 6.5 Develop Schedule		6.6 Control Schedule	
7. Project Cost Management		7.1 Plan Cost Management 7.2 Estimate Costs 7.3 Determine Budget		7.4 Control Costs	
8. Project Quality Management		8.1 Plan Quality Management	8.2 Manage Quality	8.3 Control Quality	
9. Project Resource Management		9.1 Plan Resource Management 9.2 Estimate Activity Resources	9.3 Acquire Resources 9.4 Develop Team 9.5 Manage Team	9.6 Control Resources	
10. Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 Monitor Communications	
11. Project Risk Management		11.1 Plan Risk Management 11.2 Identify Risks 11.3 Perform Qualitative Risk Analysis 11.4 Perform Quantitative Risk Analysis 11.5 Plan Risk Responses	11.6 Implement Risk Responses	11.7 Monitor Risks	
12. Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
13. Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder Engagement	13.3 Manage Stakeholder Engagement	13.4 Monitor Stakeholder Engagement	



Change Management in Agile and Waterfall

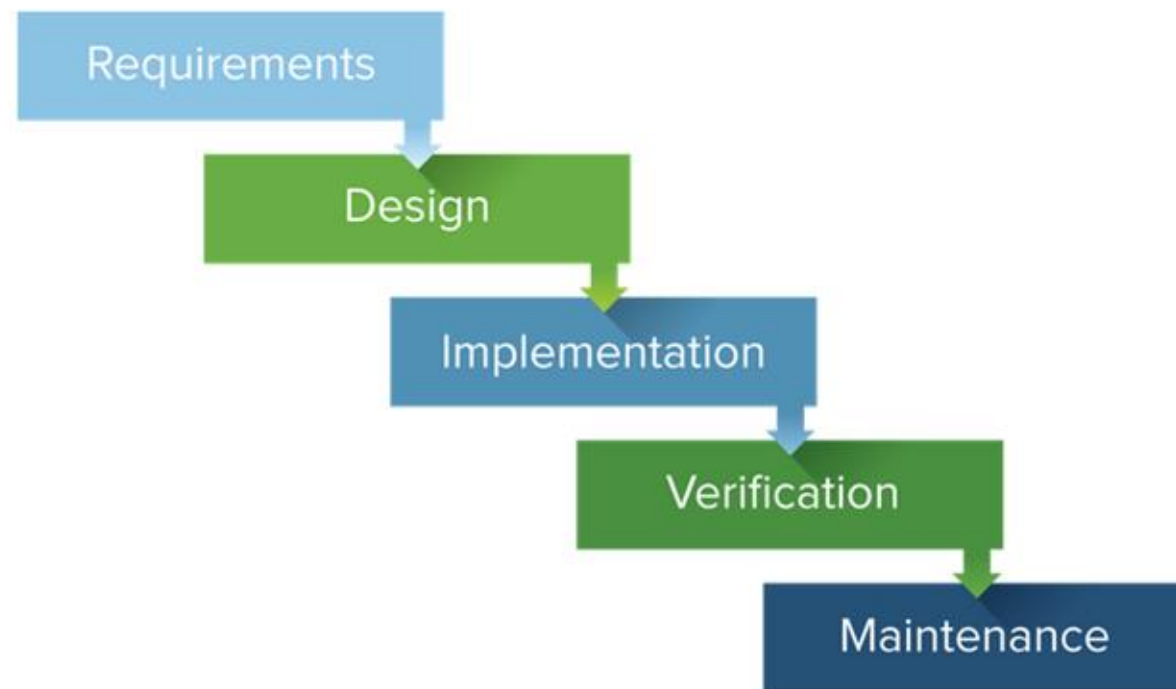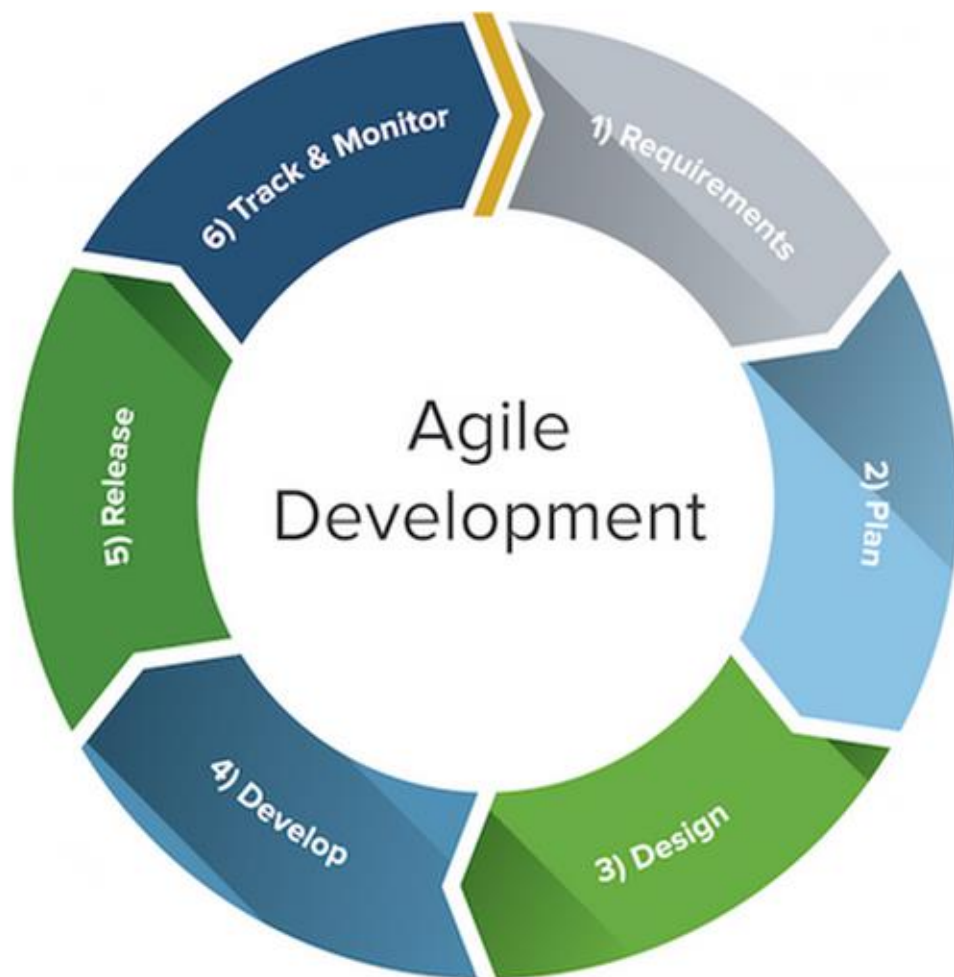

Scope changes in Waterfall

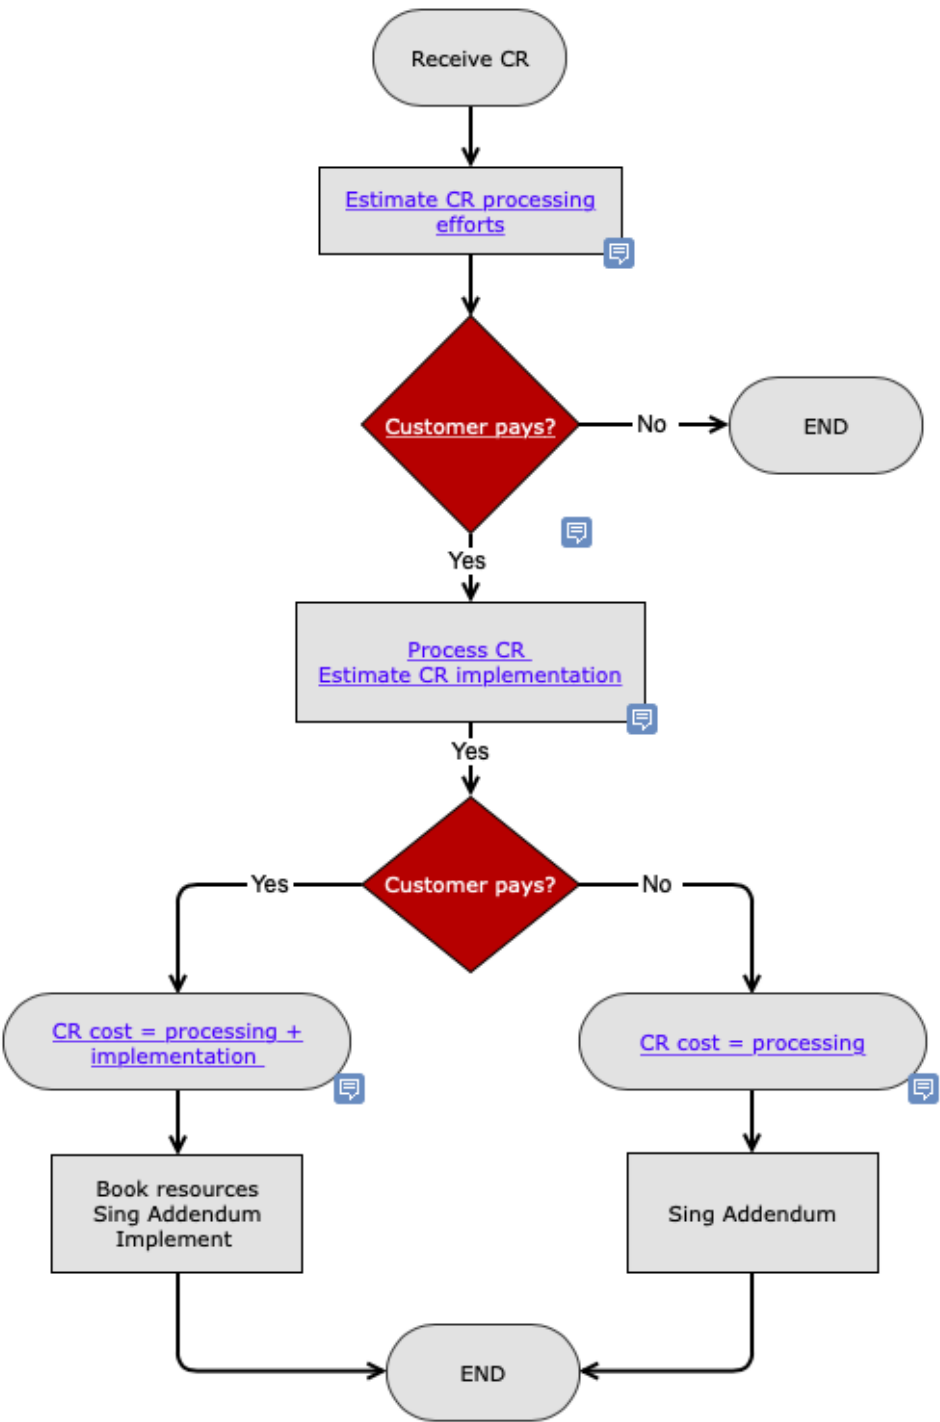


Change register

- ❖ Nature of the change
- ❖ Impact of the change (estimation/cost, duration/dates)
- ❖ Status of the approval
- ❖ Change implementation schedule and date (if any)
- ❖ Current status of all changes



Change register

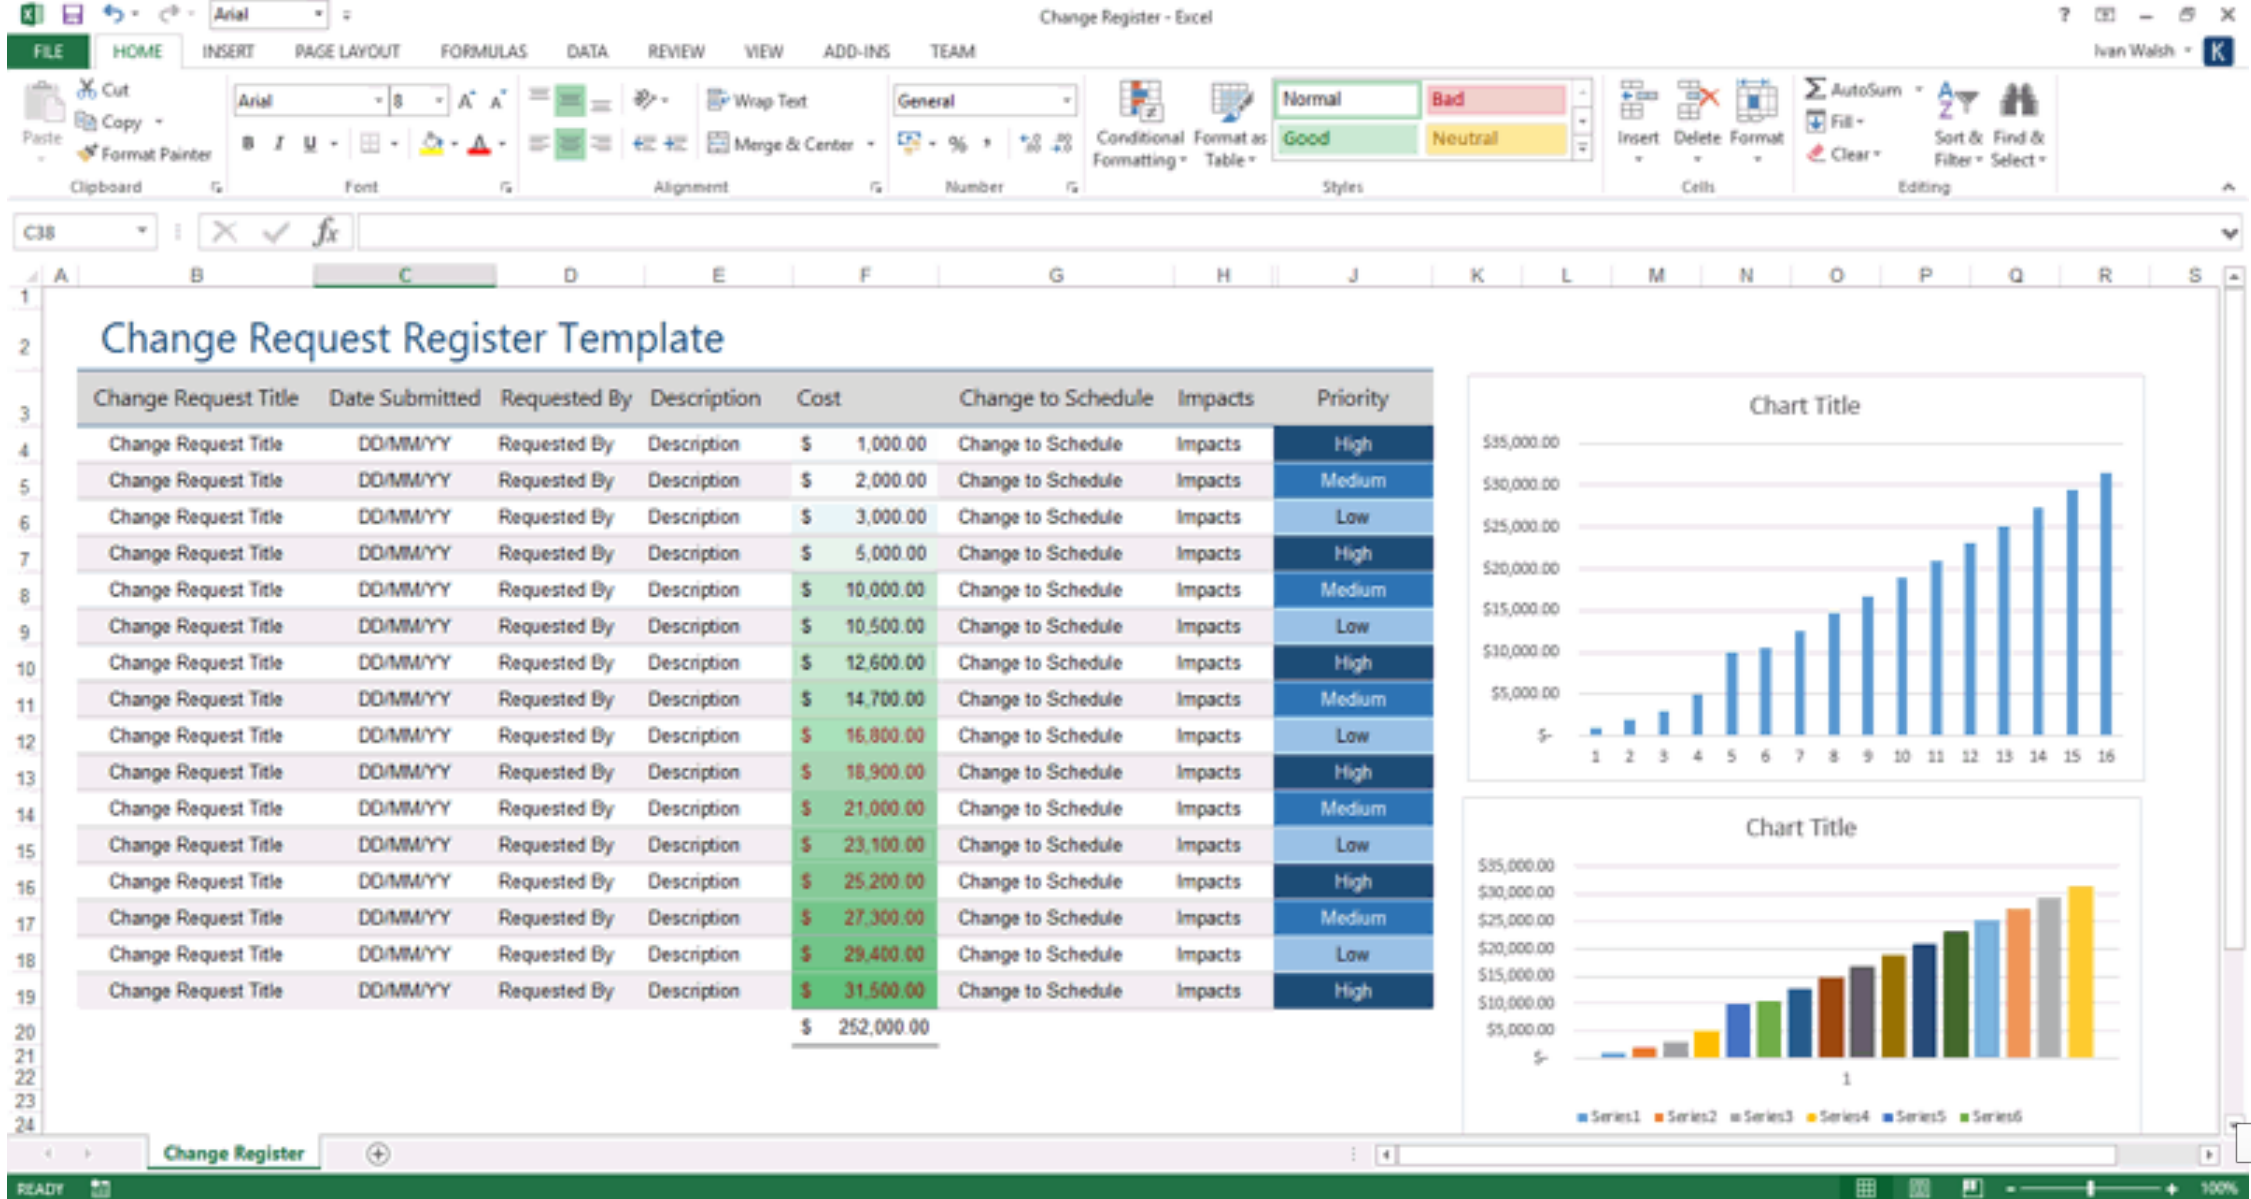

Change report

- ❖ Summary of all modifications, change proposals and issues that are currently active
- ❖ Change budget summary
- ❖ Risks related to the change
- ❖ Impact on Schedule
- ❖ Parties Involved



Change report

BSC Panel 301

ELEXON

Change

Process governing the code, subsidiary documents and systems.

BSC & Codes

The procedures that govern the electricity industry.

Risks

The techniques that confirm compliance or identify issues.

Committees

The groups that oversee changes and processes.

Market entry

Procedures for joining and leaving the market.

301/03 BSC Change Report: April 2020

Summary of Open Changes

Total open changes:

- Modifications – 20
- Change Proposals – 5
- Issues – 8

Modifications and Change Proposals

Initial Written Assessment:

- None

Assessment Procedure

- Next Workgroups: P376 – May, P379 – TBC, P392-24 March, P395 – TBC, P398 30 March, P399- 27 March, Issue 86 – 6 March, Issue 69- 31 March, Issue 88 W/C 27 April, Issue 89 W/C 20 April, P402
- APC: P392
- Assessment reports: P390, CP1525, CP1527, CP1528
- CPC batch: None

Report Phase

- RPC: P403, P404
- DMR: P397

Awaiting decision

- Authority: None
- Self-Governance: P400, P401

Awaiting implementation

- P354 - 1 Apr 20, 20, P388-1 Apr 20, P371 - 25 June 20, CP1522- 25 June 20, P371 - 25 June 20, CP1523 – 25 June 20, P383 – 1 Apr 21

ELEXON Report April 2020 BSC Panel Meeting

Modification Updates – up until decision

P332: Revisions to the Supplier Hub Principle			Update
Date Raised:	28 January 2016	Proposer:	Smartest Energy
Target Implementation Date:	Post 2020	Current Status:	Assessment Procedure
Latest Update:	Following the last Workgroup meeting in February 2020, ELEXON is working up business requirements and legal text.		
Next Event:	ELEXON is currently drafting legal text and a proposed side-letter which would be part of the Qualification process. The legal text will require all existing and new Meter Operator Agents (MOAs) and Data Collectors (DCs) to sign-the side letter to maintain Qualification status. The letter will require MOAs and DCs to agree to treat all appointments the same regardless of contract status, such that they meet all relevant BSC requirements. The side-letter is out for internal review and we are seeking external legal advice on this before distributing to the Workgroup.		
Issue:	The BSC when originally created was designed to support the Supplier hub principle and to this end is silent on the practice of 'Customer appointed Agents'. The 'appointment' of Agents by Customers, outside of the Supplier hub principle, makes managing Agent performance and delivery of obligations within the BSC difficult, resulting in a reduction in a Supplier's ability to manage performance against industry targets and risking non-delivery of specific obligations.		
Current Solution:	P332 proposes to amend the roles and responsibilities of Supplier Agents. This includes requiring Supplier Agents to become signatories to the Balancing and Settlement Code (BSC).		
History:	P332 was raised by Smartest Energy Limited on 28 January 2016 and seeks to address issues associated with Customer's contracting directly with Supplier Agents. The Panel, at its meeting on 14 September 2017, directed (in accordance with F2.6.10) the P332 Workgroup to pause work on the P332 solution – P332 was effectively placed on hold. The Panel believed the Significant Code Review (SCR) on Half Hourly Settlement (HHS) could change the baseline against which P332 was being developed and assessed. Periodic checkpoints were scheduled to check whether P332 should re-start, remain on-hold or be withdrawn. The Panel approved a seven-month extension to the Assessment Procedure at its meeting on 10 May 2018. The rationale for the extension was to allow enough time for the outcome of Ofgem's policy work to be known and for the Target Operating Models (TOMs), which are being developed as part of the SCR, to be further developed. The Panel approved a nine-month extension to the P332 Assessment Procedure at its meeting on 13 December 2018, returning with the Assessment Report to the September 2019 Panel meeting. This was on		



Why changes are tough



70%

FAILURE



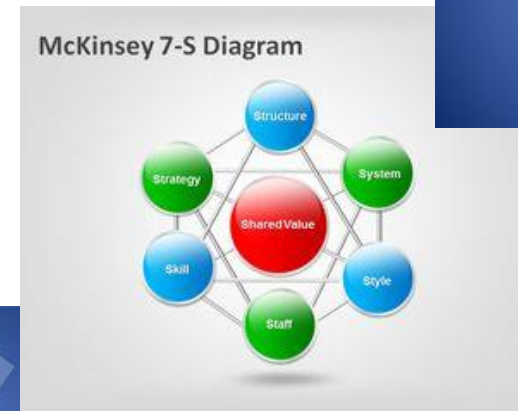

What matters?

- ❖ Background (personal + organizational)
- ❖ Environment (culture, business domain etc.)
- ❖ Nature of the change
- ❖ Consequences of the change
- ❖ Stakeholders' personalities





Resistance level (Maurer)



- I. I don't understand
- II. I don't like **It**
- III. I don't like **Him**



Why people resist change

REASONS FOR RESISTANCE

- ❖ Changes take time and efforts
- ❖ People tend to be conservative and passive
- ❖ Fear of loss (control, status, uncertainty)
- ❖ Negative personal experience
- ❖ Alterations in a person's duties, powers, and influence

RESISTANCE TYPES

- ❖ Logical
- ❖ Psychological
- ❖ Sociological



Resistance to Change: Action Plan

Logical

- ❖ Get a detailed picture of concerns
- ❖ Adjust business processes to the change
- ❖ Increase transparency

Psychological

- ❖ Support in obtaining new skills
- ❖ Make learning as easy as possible
- ❖ Make change positive


Sociological

- ❖ Highlight their importance
- ❖ Work out opportunities to save their status
- ❖ Discuss new opportunities



The Kübler-Ross Change Curve

Emotional Response to Change

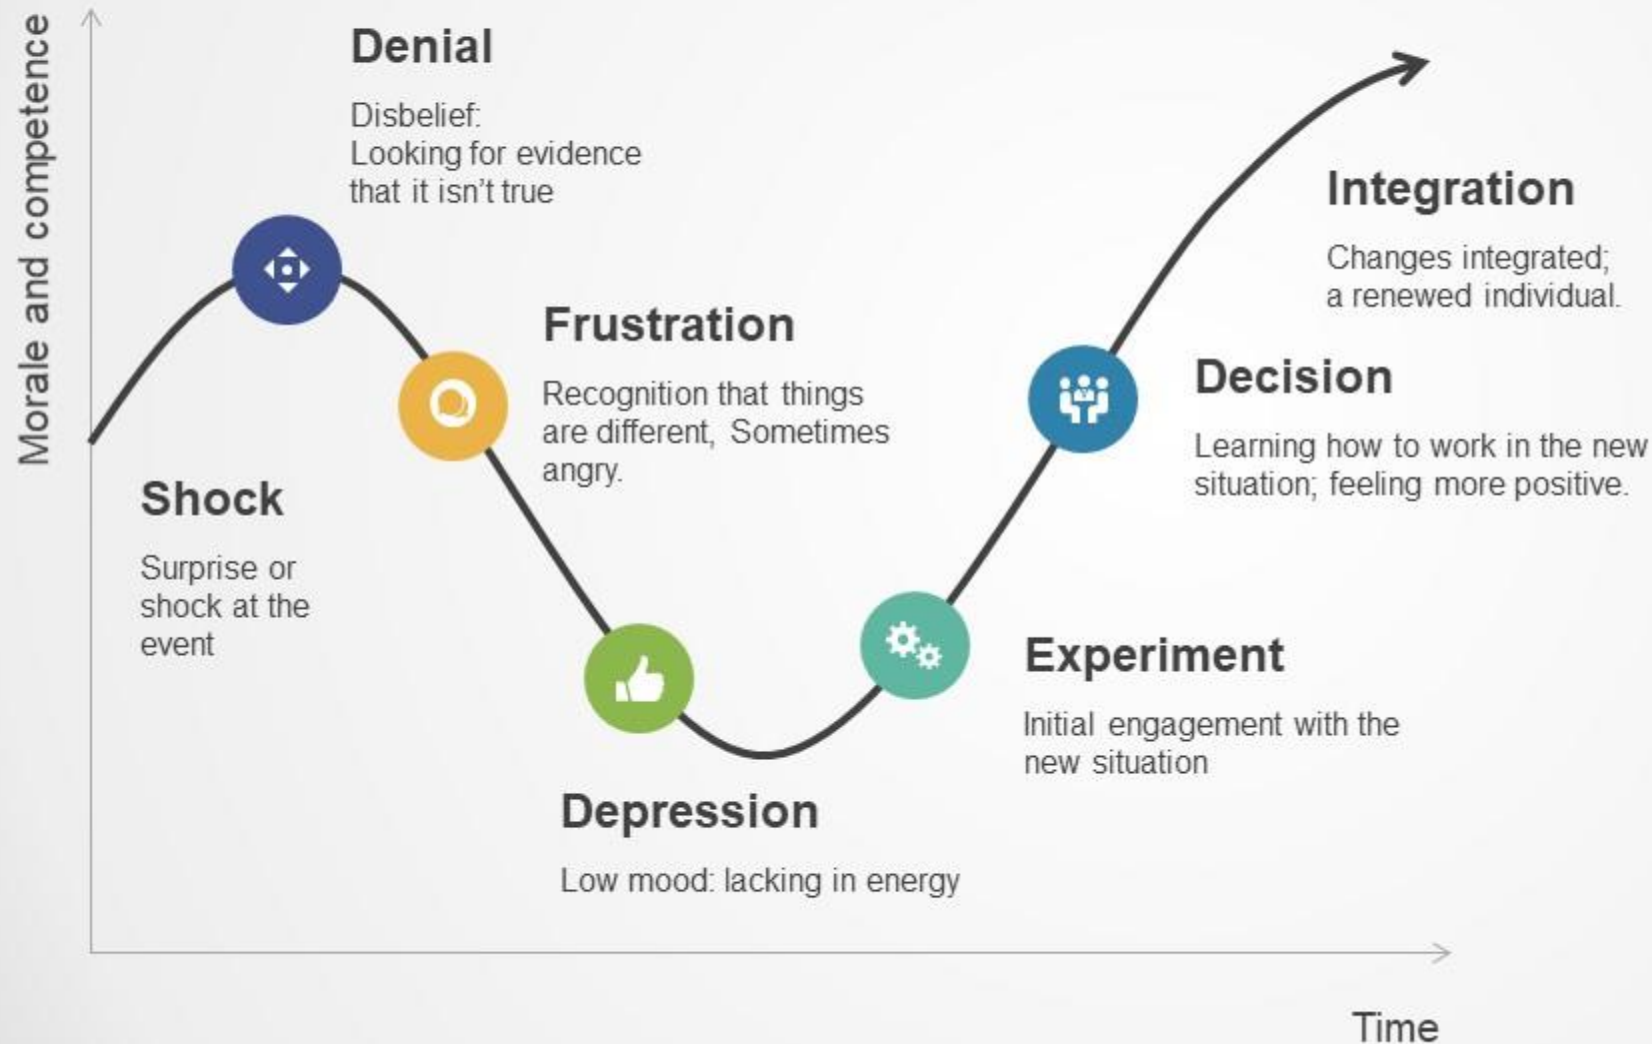

Creative Alignment

Maximize Communication


Spark Motivation

Develop Capability


Share Knowledge



Change Curve: Action Plan

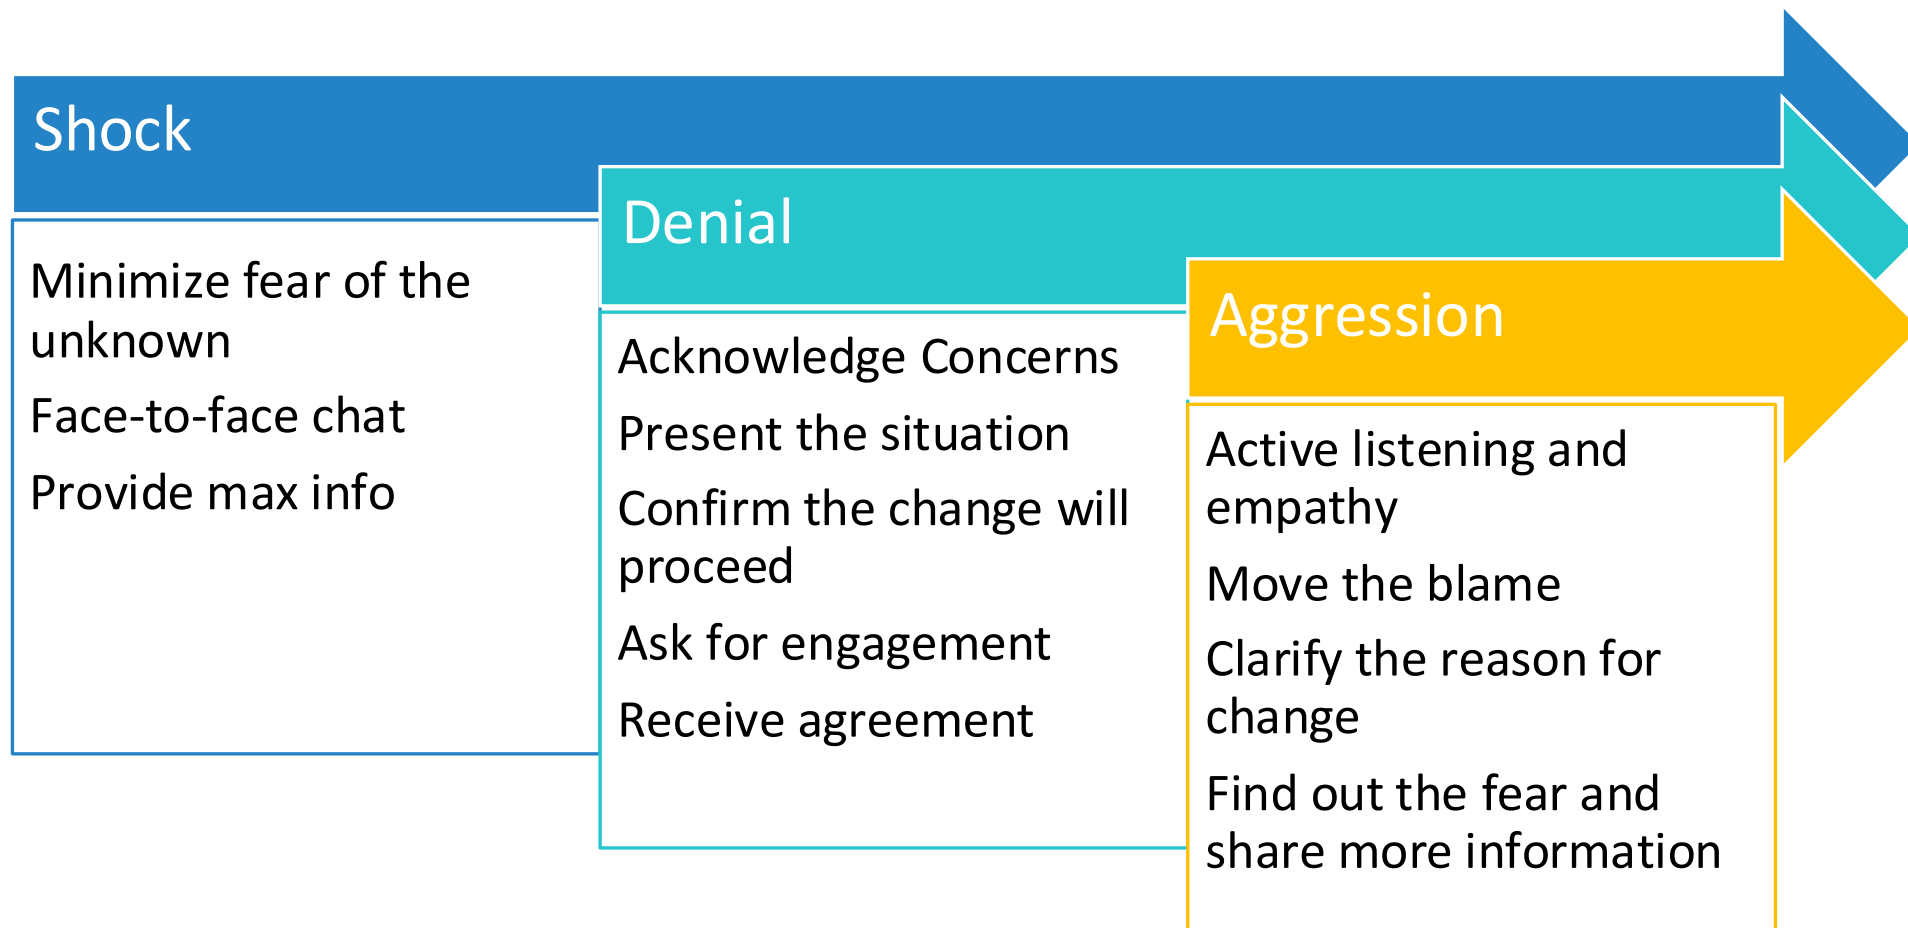

Change Curve: Action Plan

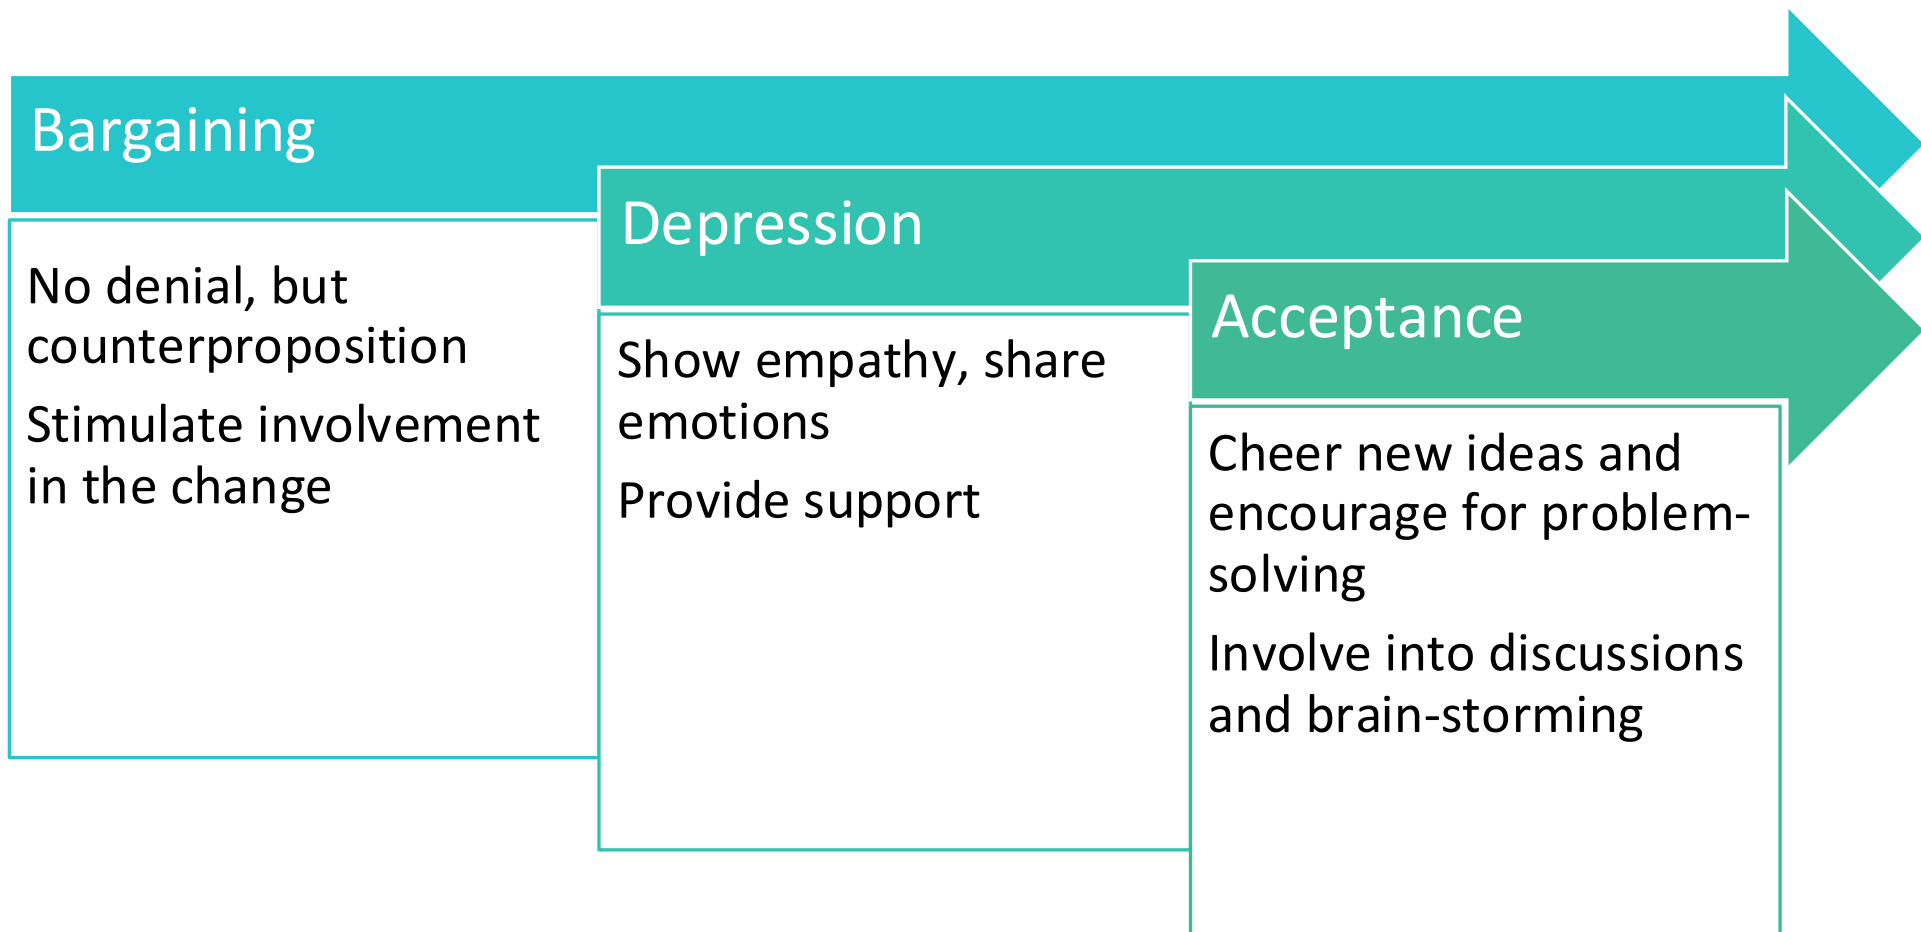

Managing Resistors

ACTIVE RESISTOR

1. Listen and react constructively
2. Help to understand the change
3. Make it clear what we cannot control


4. Create an open environment for resistors to feel safe and express their opinion freely

PASSIVE RESISTOR

1. Check their reaction vs action
2. Use facilitation technics (e.g. ask everyone to right down pros and cons of the change)
3. Use your supporters to find passive resistors



Force Field Analysis

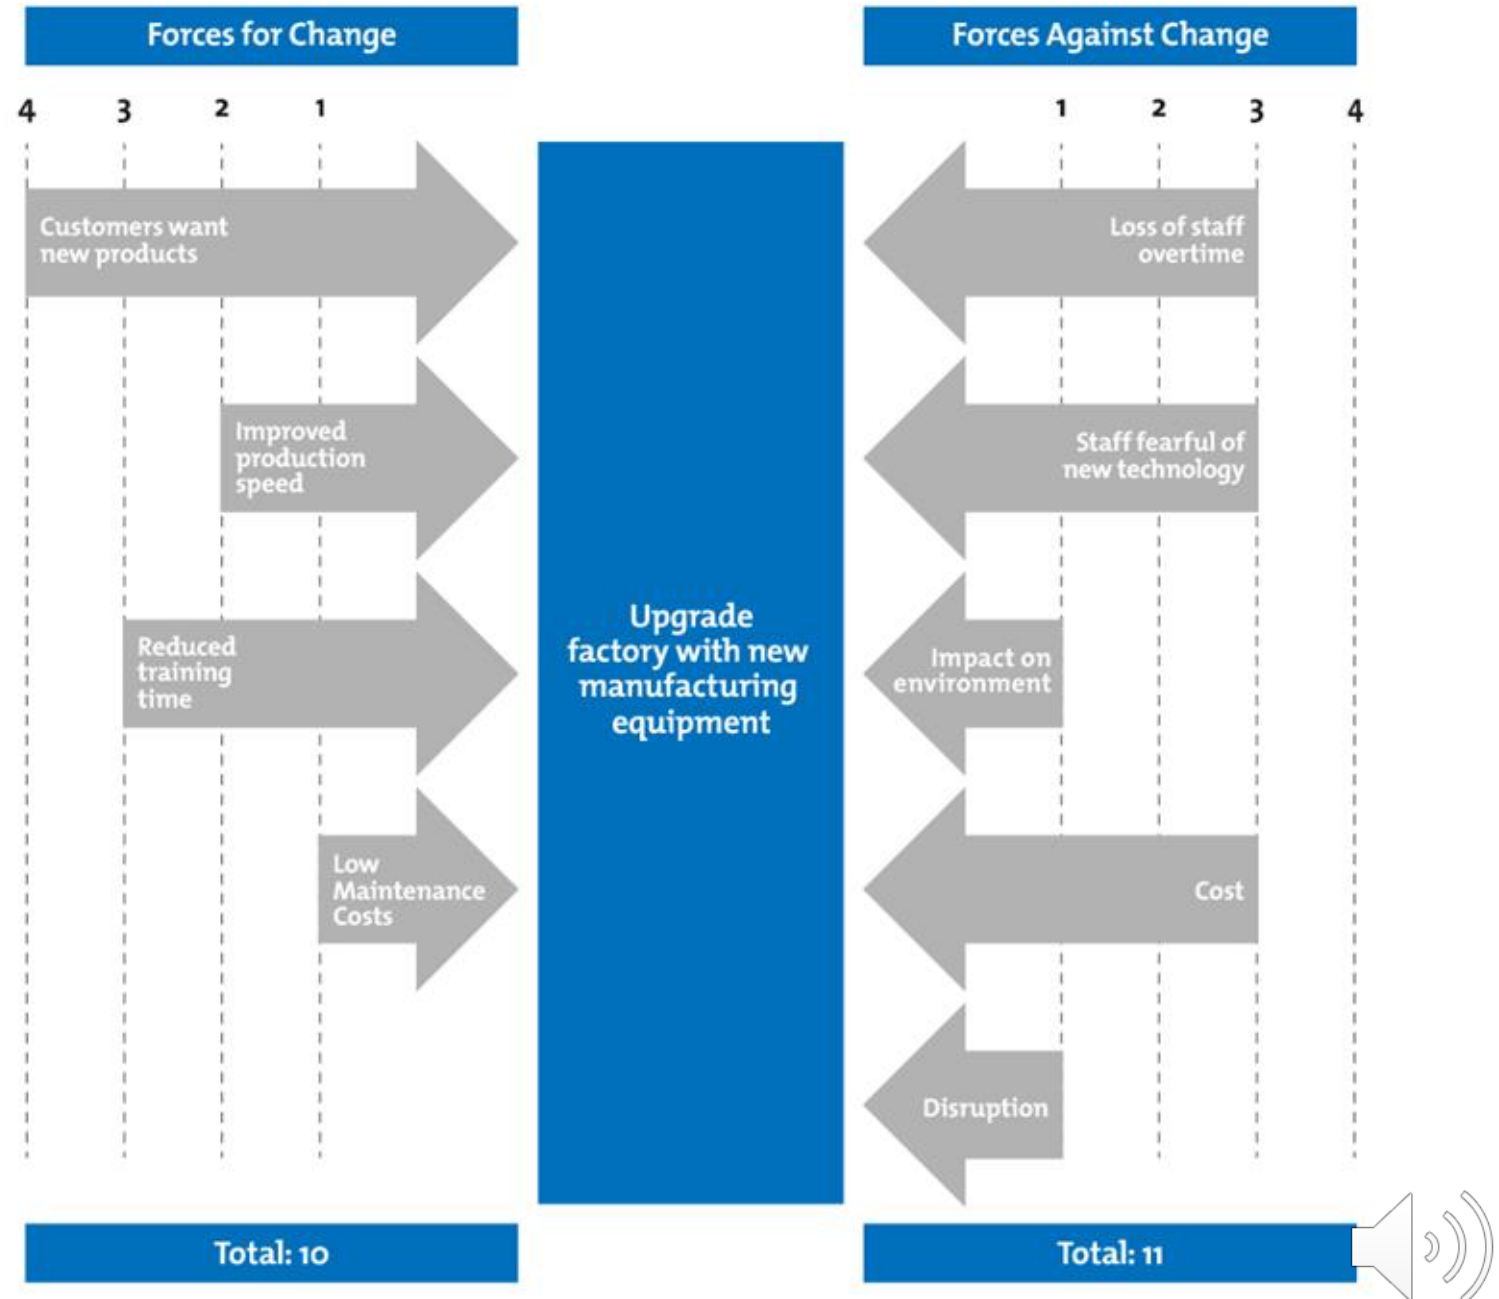

Force Field Analysis: Action Plan

- ❖ Listen to the stakeholders and identify initial reasons for resistance, consider all parties involved
- ❖ Ensure that the management board (and informal leaders) support the change
- ❖ Mitigate resistance, enforce support. Add learning plan, work with personal fears,
- ❖ Update Stakeholder Register, Communication and Risk plans
- ❖ Collect feedback and provide regular updates



Key Change Management Roles



Sponsor



Project
Manager



Change Agent



Project Lifecycle

